



SOUL KATANA

Network Cabling for ASNB Kota Bharu Kelantan - Work Order DC10/006


Report Period of 16/09/2022 - 05/12/2022

Date	Description
16/09/2022	Observation and taking note of current network/server rack



SOUL KATANA

Date	Description
------	-------------

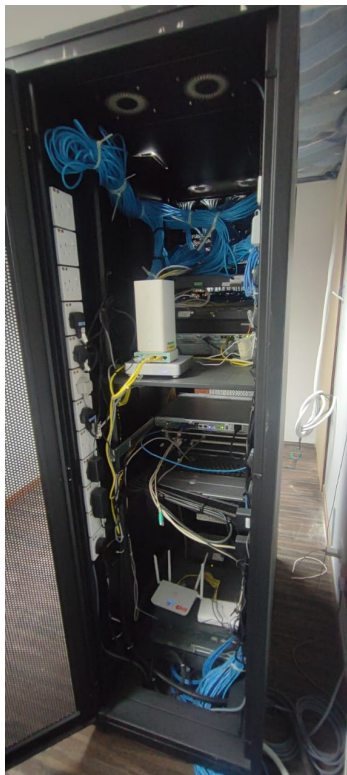

16/09/2022	We discover floor trunking is not ready due to work debris that has yet to be cleared by turnkey contractor.
------------	--



SOUL KATANA

Date **Description**



17/09/2022 Server room layout needs to be altered as to affirm server rack position

17/09/2022 Network trunking is overlapping with electrical. Need to reconcile with M&E provider.

SOUL KATANA


Date **Description**






SOUL KATANA

Date	Description
------	-------------

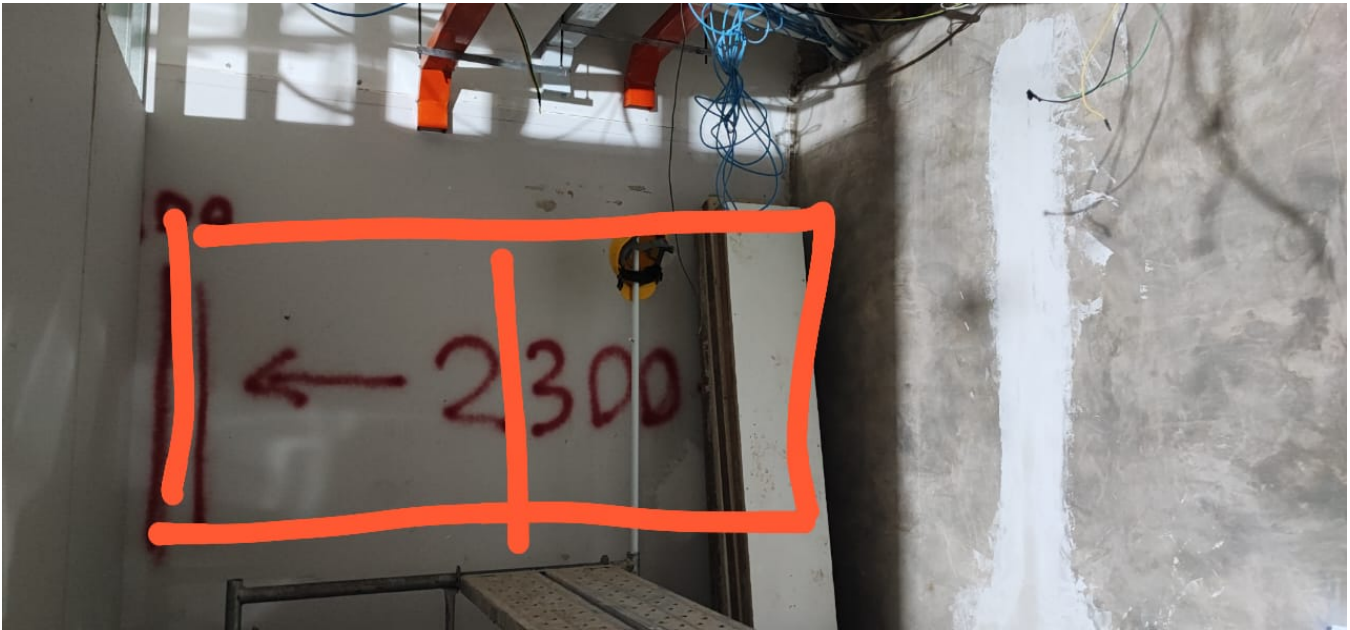


18/09/2022	Reproduced schematics with color codes to distinct materials of installations.
------------	--

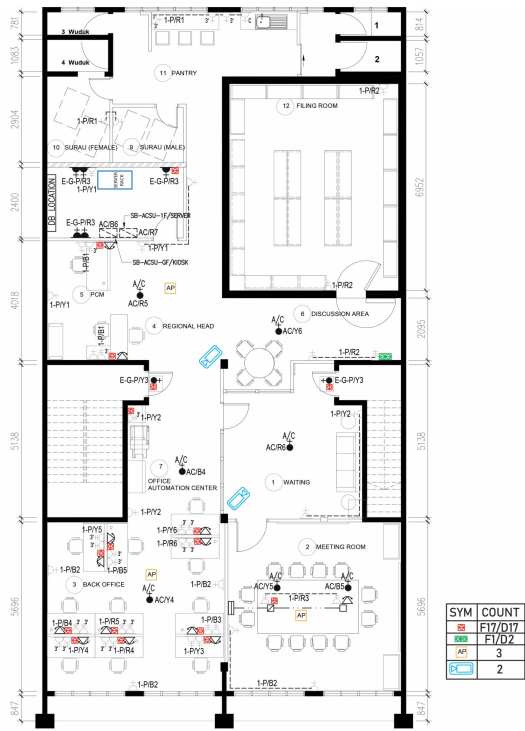


SOUL KATANA

Date	Description
------	-------------

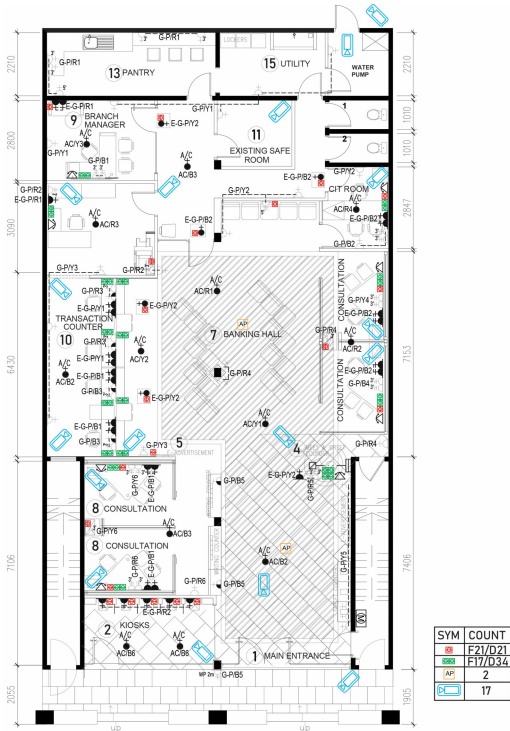


Ground Floor Plan - FACEPLATES & DATA POINTS
Scale 1:150 (A3)

19/09/2022	Server/network rack placement discussion and reconciliation.
------------	--

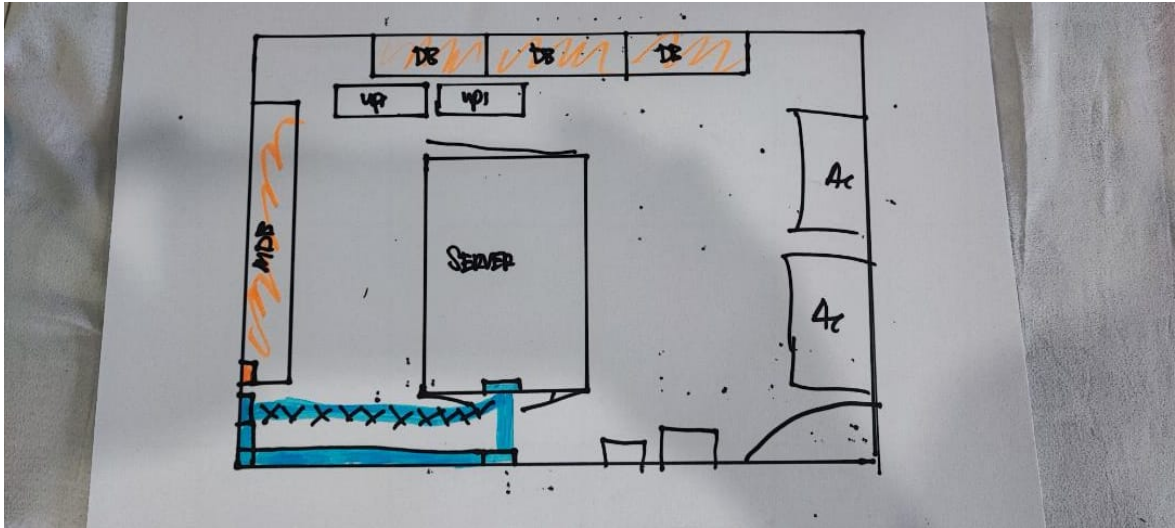

SOUL KATANA

Date Description

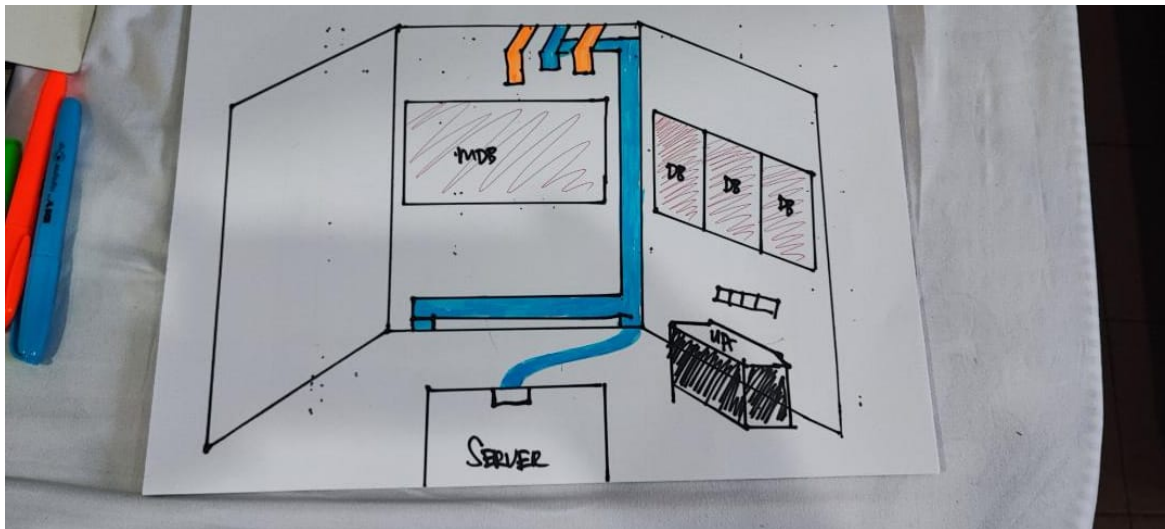

19/09/2022 Floor trunking ready to deploy.






Date **Description**



20/09/2022 First floor network cabling successfully done and secured.

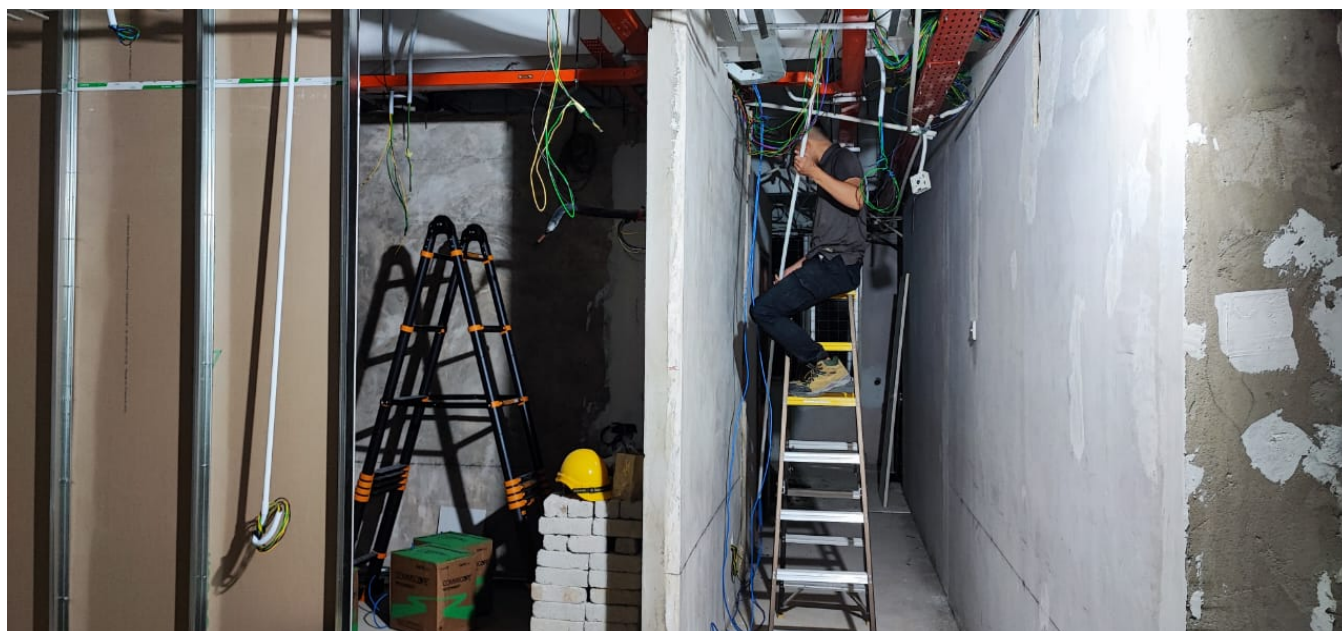

SOUL KATANA

Date **Description**



SOUL KATANA


Date

Description



SOUL KATANA

Date **Description**

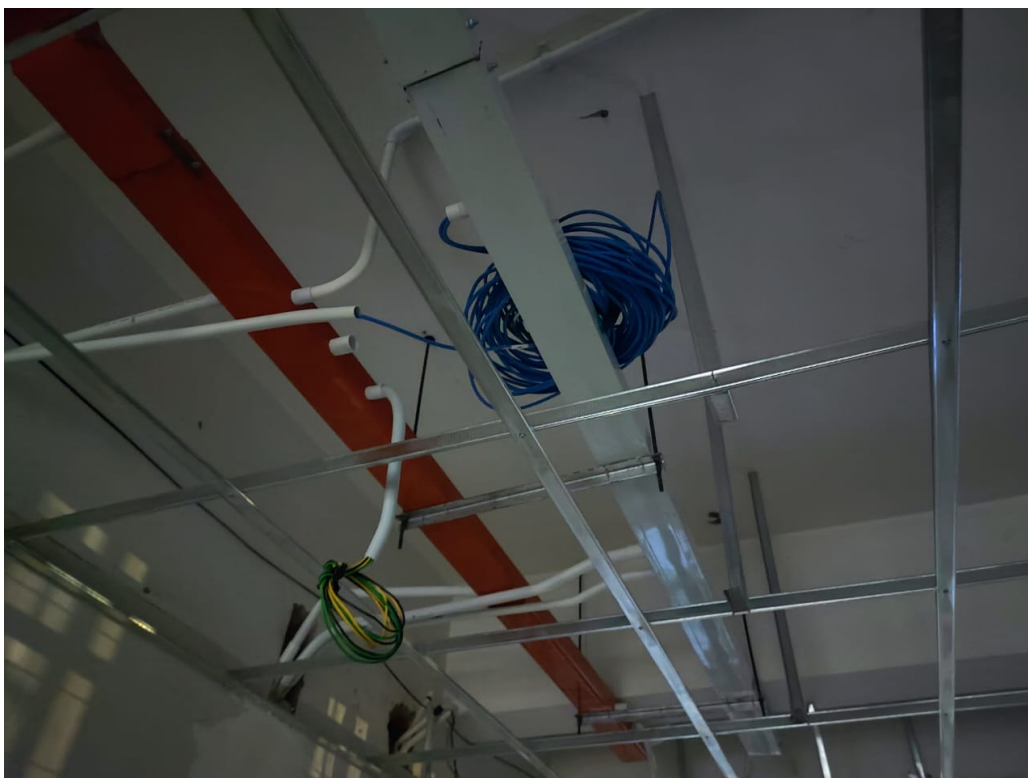

SOUL KATANA

Date **Description**




21/09/2022 Ground floor cleanup ready. Partition marking done.



SOUL KATANA


Date	Description
22/09/2022	Partition structure ready. Still wait for M&E to provide trunking+pipings.
23/09/2022	Discuss on part of telephone infra and clear up on CCTV cabling.
24/09/2022	Piping insertion, rearrangement, concealing and outlet exiting.

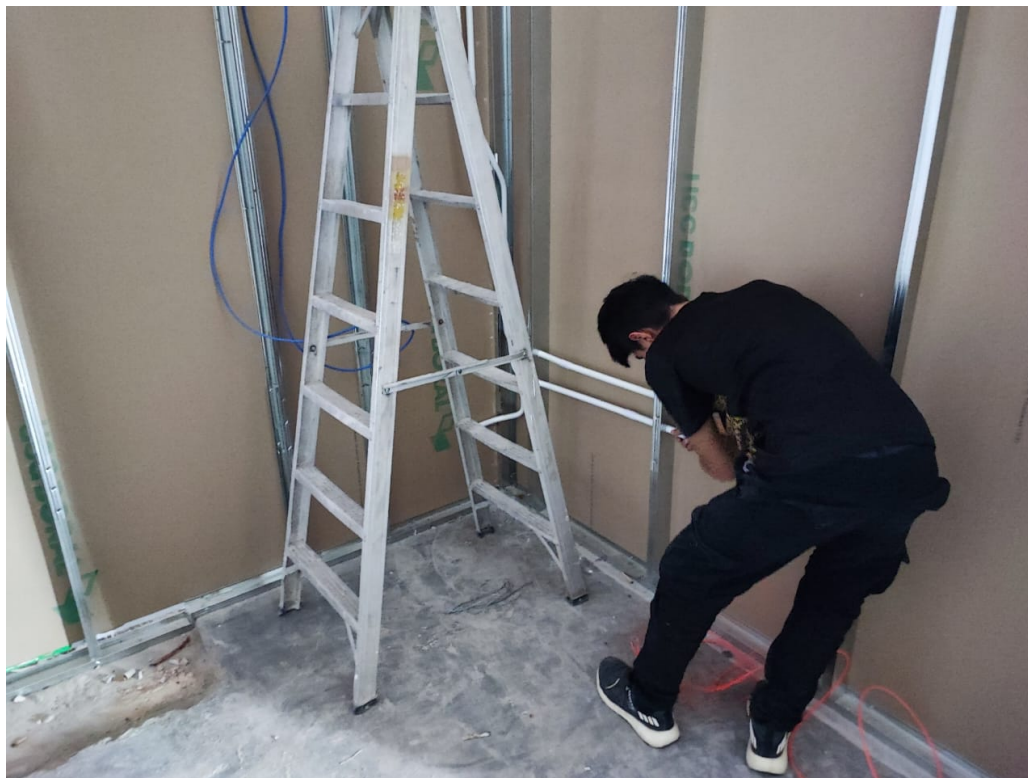




Date

Description

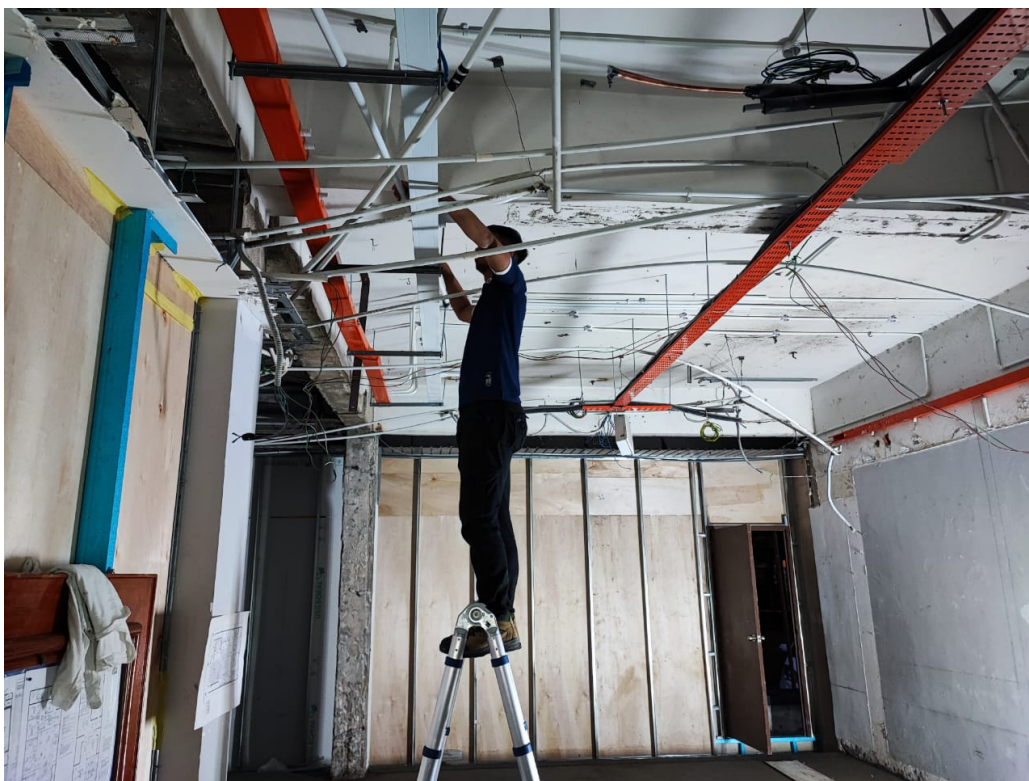

SOUL KATANA

Date **Description**

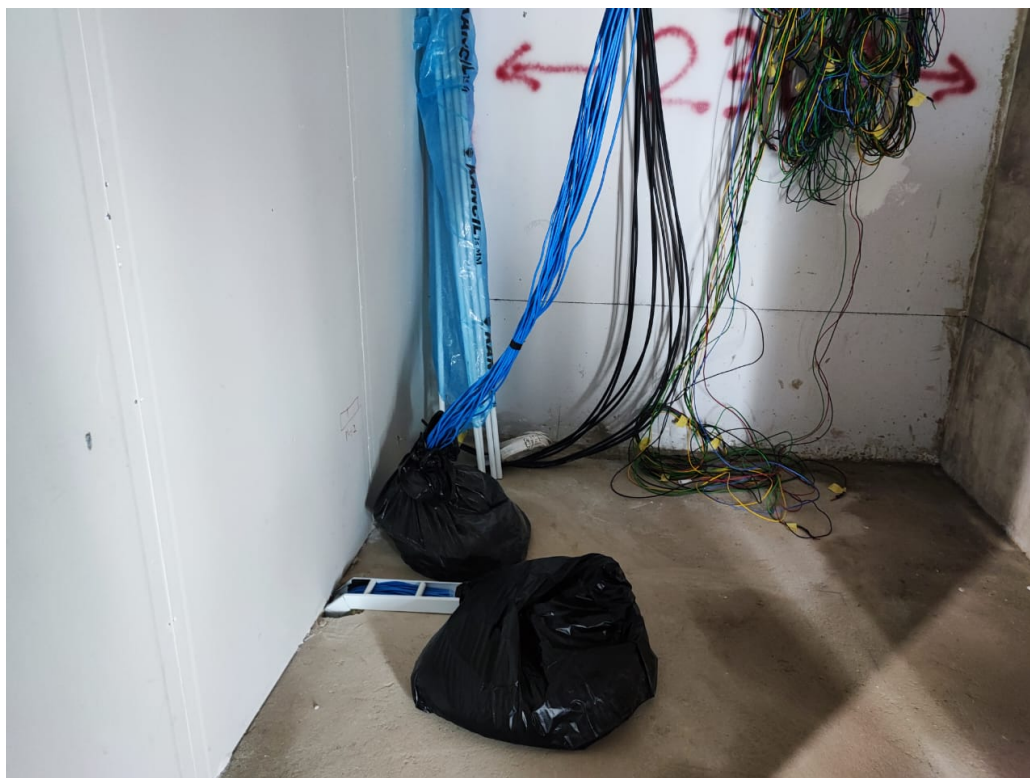




Date	Description
------	-------------




SOUL KATANA

Date **Description**

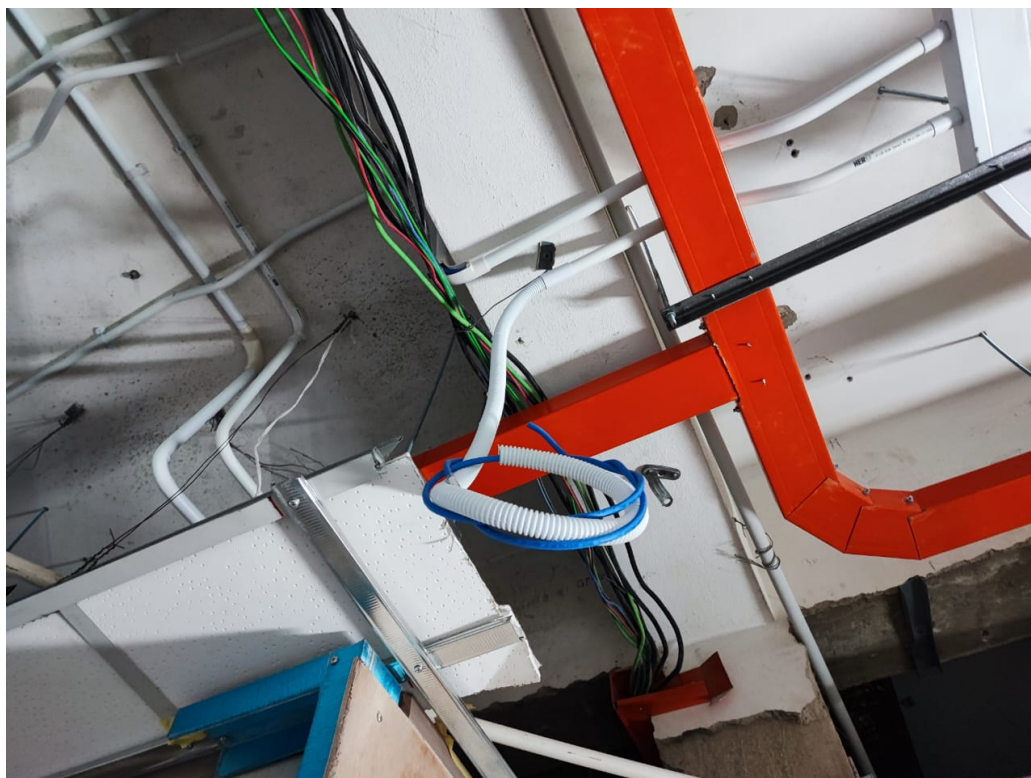



Date **Description**

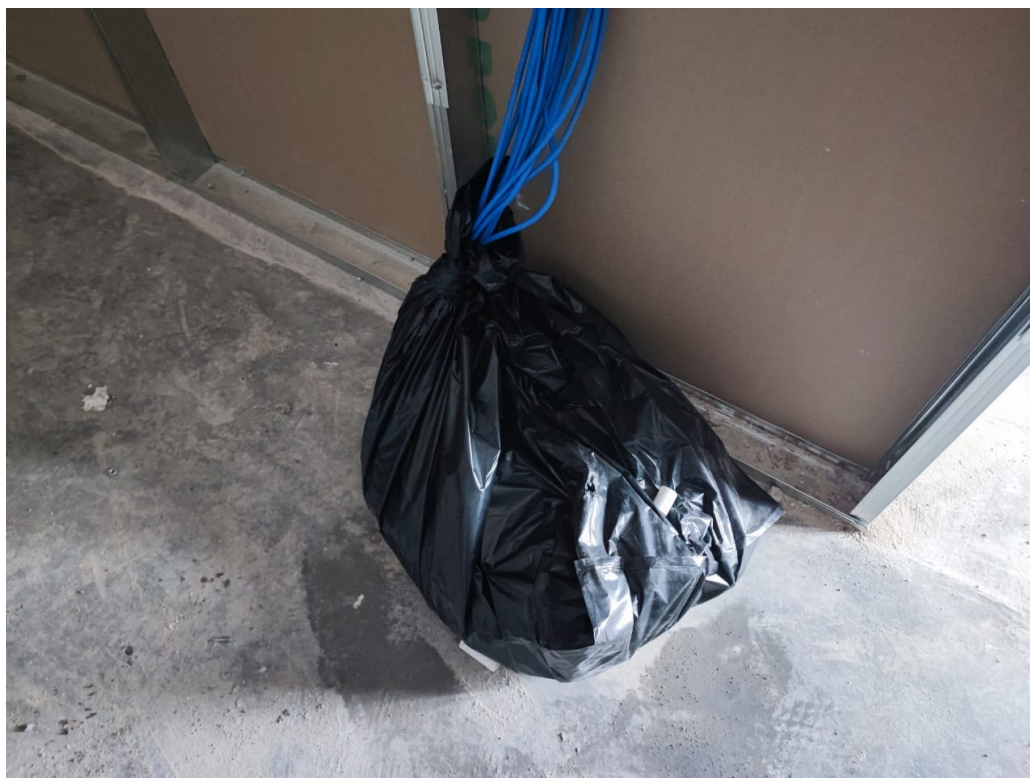

16/10/2022 Faceplate installation, termination and labelling.



SOUL KATANA

Date **Description**



SOUL KATANA

Date **Description**



SOUL KATANA


Date **Description**



- | | |
|------------|---|
| 17/10/2022 | Received a very bad news from rack factory. Because of insufficient material, the new delivery date will be on the 3rd of November 2022. Advised project management and ready to negate termination on the legacy rack temporarily with help from Heitech Padu. |
| 19/10/2022 | Have a problem with point C15. Apparently the cable has been punctured from outside by cabinet worker even though stern warning has been issued earlier. Referred to project management. As of now need to wait. |

SOUL KATANA

Date **Description**

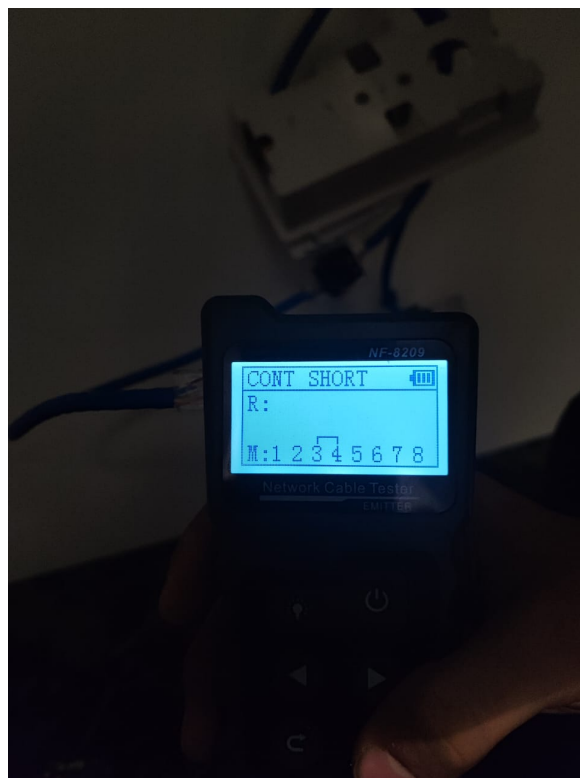

20/10/2022	No decision made. Proceed to use splitter on point C15 and C16. Impossible to cut open the conceal cabinet to attend to cables at this moment.
21/10/2022	Temporary network termination at the legacy rack deployed successfully.

SOUL KATANA

Date Description



SOUL KATANA


Date	Description
	
	

SOUL KATANA

Date **Description**



21/10/2022 Variable order of 2 horizontal cablings - ST3 and TC

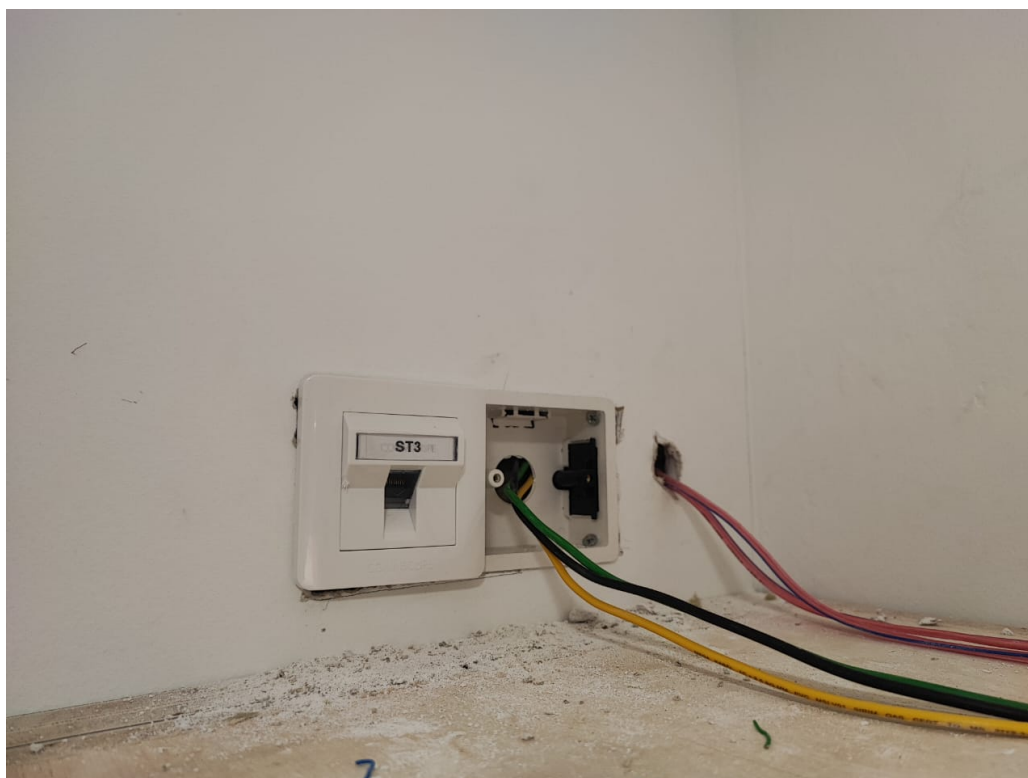

SOUL KATANA

Date **Description**



06/11/2022 Resuming cable pull exercise for Phase 2





Date **Description**



17/11/2022 Variable order of 2 horizontal cablings - S2 and ST4





Date **Description**




29/11/2022 Engage Fluke testing for all points.

SOUL KATANA

Date

Description

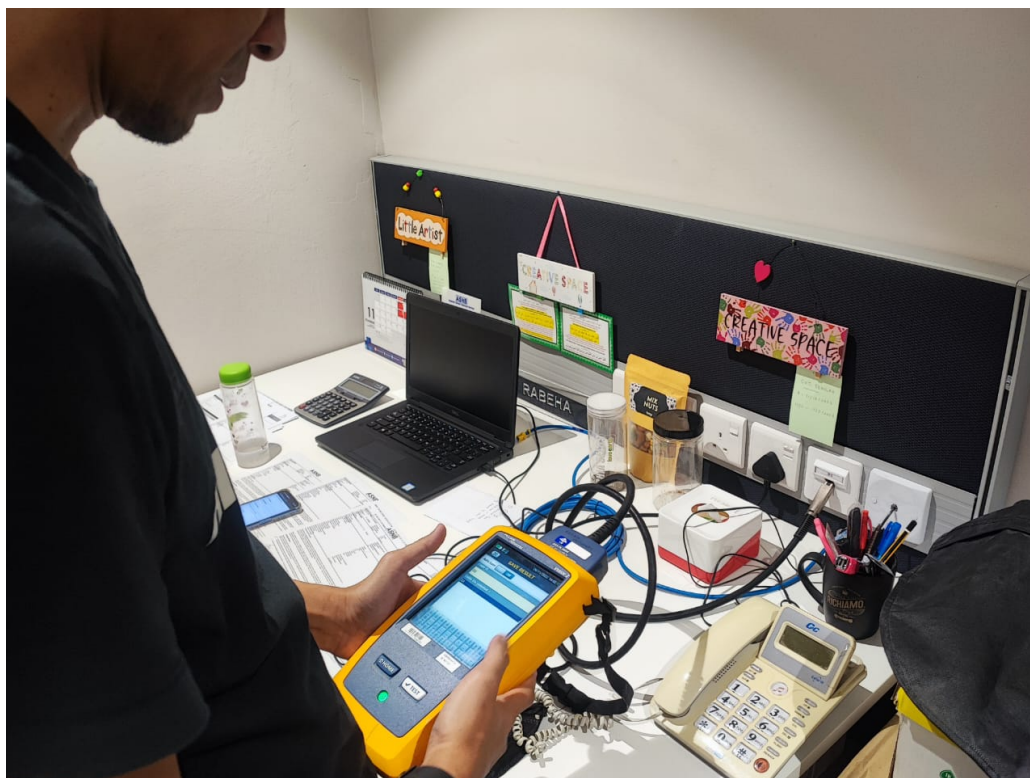



Date **Description**



02/12/2022 Cable trunking descents at Server Room been finalized and concealed.

